CARES ACT


K12 WIRELESS IMPROVEMENTS

MEETING#5



AGENDA


- Review Dashboard
- Past due
- Priority of the week
- Issues/Risk Log
- Needs assessment
- Communications
- Q & A



EQUIPMENT ORDERED

PAST DUE

- Who needs help?
- What can we do?

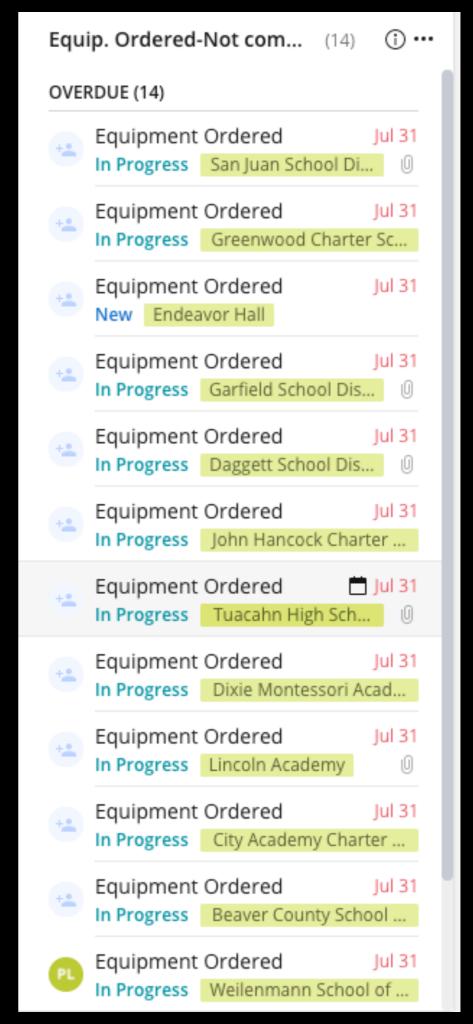

EQUIPMENT DELIVERED

PAST DUE

- Update status
 - Partial order in = In Progress
 - Complete order in = Completed

| Equip. Delivered - New (78) | | | | |
|-----------------------------|--|------------------|--|--|
| OVE | RDUE (78) | | | |
| +_• | Equipment Delivered New Mountainville Academy | Aug 21 | | |
| + | Equipment Delivered New Millard School District | Aug 21 | | |
| + | Equipment Delivered New Excelsior Academy | Aug 21 | | |
| + | Equipment Delivered New Channing Hall | Aug 21 | | |
| + | Equipment Delivered New San Juan School District | Aug 21 | | |
| + | Equipment Delivered New Greenwood Charter Scho | Aug 21 | | |
| + | Equipment Delivered New Utah County Academy of | Aug 21 f Scie | | |
| + | Equipment Delivered New Merit Preparatory Acade | Aug 21 | | |
| + | Equipment Delivered New C.S. Lewis Academy | Aug 21 | | |
| + | Equipment Delivered New Bonneville Academy | Aug 21 | | |
| +* | Equipment Delivered New Wasatch Charter School | Aug 21 | | |
| + | Equipment Delivered New Lakeview Academy | Aug 21 | | |

PROJECT DASHBOARD

17 WEEKS LEFT!!!

Priority this week



| +* | Equipment | Installed & C | Sep 4 |
|-----|-------------|-----------------------|-------|
| | In Progress | Monticello Academy | |
| + 0 | Equipment | Installed & C | Sep 4 |
| | In Progress | Sevier School Distric | t |
| +•• | Equipment | Installed & C | Sep |
| | In Progress | American Preparato | ry A |
| +* | Equipment | Installed & C | Sep |
| | In Progress | Salt Lake City Schoo | l Dis |
| +* | Equipment | Installed & C | Sep |
| | In Progress | Ogden Preparatory | Acad |
| +* | Equipment | Installed & C | Sep |
| | In Progress | Alpine School Distric | t |
| +* | Equipment | Installed & C | Sep |
| | In Progress | Granite School Distr | ict |
| | Equipment | Installed & | Sep 1 |
| +* | In Progress | | nal |

| Equip Installed - New (117) | | | | |
|-----------------------------|---|-------|--|--|
| NEW (117) | | | | |
| +* | Equipment Installed & New Logan City School District | Sep 4 | | |
| +• | Equipment Installed & New Mountainville Academy | Sep 4 | | |
| +• | Equipment Installed & New Millard School District | Sep 4 | | |
| +• | Equipment Installed & New Entheos Academy Kearns | Sep 4 | | |
| +• | Equipment Installed & New Entheos Academy Magna | Sep 4 | | |
| +• | Equipment Installed & New Excelsior Academy | Sep 4 | | |
| +• | Equipment Installed & New Channing Hall | Sep 4 | | |
| + | Equipment Installed & New San Juan School District | Sep 4 | | |
| + | Equipment Installed & New Greenwood Charter Schoo | Sep 4 | | |
| +* | Equipment Installed & New Utah County Academy of S | Sep 4 | | |
| +* | Equipment Installed & New Merit Preparatory Academ | Sep 4 | | |
| +• | Equipment Installed & New American Leadership Acad | Sep 4 | | |




Needs assessment - PDF documentation

K12 WIRELESS IMPROVEMENTS


COMMUNICATION

PROJECT WIKI

Find the FAQ, links, meeting presentations, meeting agenda.



<u>UEN.ORG</u> - CARES ACT K12 WIRELESS IMPROVEMENTS



K12 WIRELESS IMPROVEMENTS

Q&A

